


Kanopolis

2019 – 33' above MPP
3rd highest pool of record



Rock and Silt Removal

Completed. Fall 2019

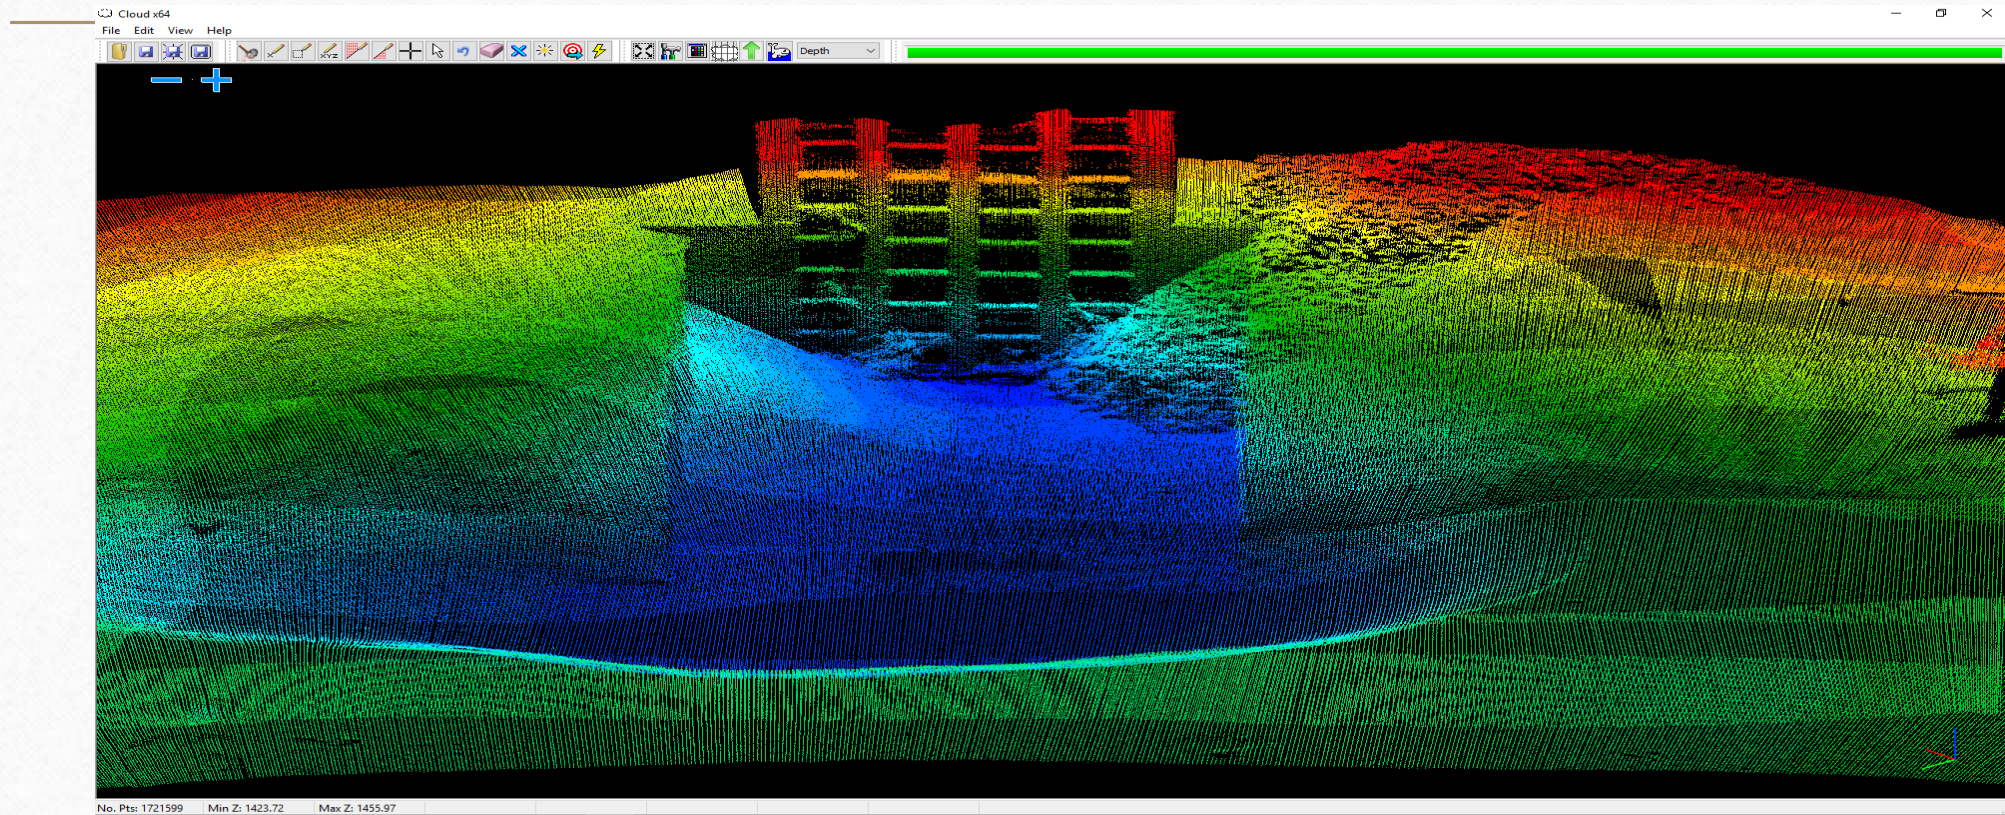

Service Gate Replacement

2 gates

Contractual Completion Date – September 2019


Revised Completion Target - 31 March 2020



Trash Rack Replacement

Fabrication and Delivery Complete

Installation target: 31 March 2019

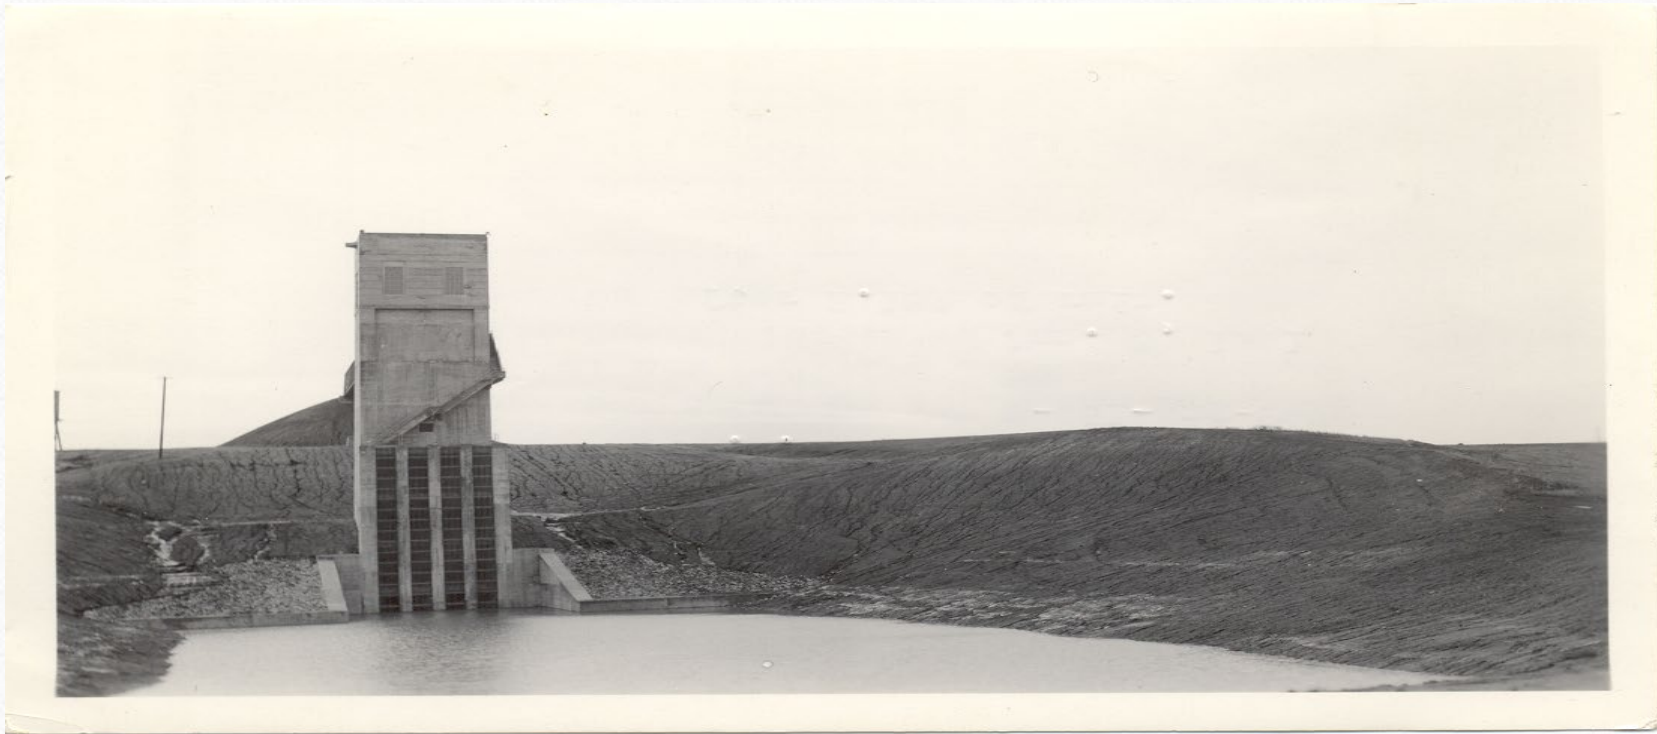

Outlet Channel Slide

Repair Completion Target – Fall 2020



Upcoming Construction Work

- Spring 2020
 - Embankment Collector System replacement
- Fall/Winter 2020
 - Embankment debris removal
 - Embankment Rip Rap overlay
 - Intake Tower Service Bridge repair/painting
